



TCR Impact Sheets

Date: September 2023
Version 1.01



Funded by the
European Union

Impact sheets for selected major Temporary Capacity Restrictions (TCR)

Foreword

On RFC North Sea – Baltic we introduced the **TCR Impact sheets** to present in one glance general and important information about upcoming TCRs. These impact sheets highlight **some infrastructure works which have a big impact** on international rail freight traffic along RFC North Sea – Baltic.

Disclaimer:

The content of this document has been compiled with meticulous care based on information available at the publication date. However we cannot assume any liability for accuracy and accept no liability for damages suffered as a result of defects of this document.

For detailed and complete customer information we kindly refer to the information which is available via the involved national Infrastructure Managers.

Further information (e.g. in form of an excel list on all planned TCR) is available on the website of RFC NS-B under link: <http://rfc8.eu/customer/temporary-capacity-restrictions/>


Version 1.1 for timetable 2023, 2024 and 2025

Publication Date: September 2023

Impact of TCR TT 2023 at Infrabel

Section Antwerpen-Montzen

Map view

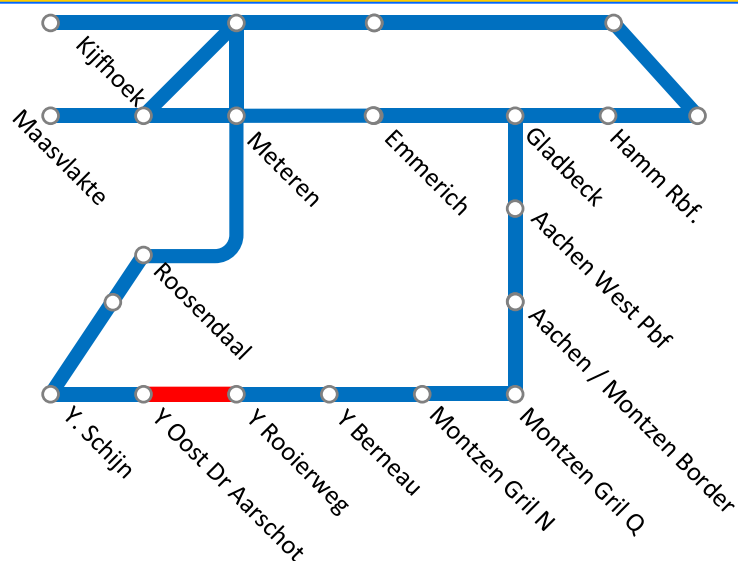

Impact on International Rail Freight

- Deviations: L24/1-L40-L36A-L36
- Estimated extra running time: TbD
- Restrictions for ad-hoc requests: no
- Restrictions in train parameters: no
- Restrictions in container profile: no
- In annual timetable: no, timetables adapted at the latest 4 weeks before operation

Major Capacity Restriction

- Section: Aarschot - Hasselt
- Typ: Total Closure
- Period: 28.10.2023 (00:00) – 06.11.2023 (4:00)
- Type of works: Signalling ETCS

2023 Calendar

■ Single track operation ■ Total closure

January						
Su	Mo	Tu	We	Th	Fr	Sa
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30	31				

February						
Su	Mo	Tu	We	Th	Fr	Sa
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28				

March						
Su	Mo	Tu	We	Th	Fr	Sa
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

April						
Su	Mo	Tu	We	Th	Fr	Sa
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30						

May						
Su	Mo	Tu	We	Th	Fr	Sa
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30	31			

June						
Su	Mo	Tu	We	Th	Fr	Sa
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	

July						
Su	Mo	Tu	We	Th	Fr	Sa
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30	31					

August						
Su	Mo	Tu	We	Th	Fr	Sa
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		

September						
Su	Mo	Tu	We	Th	Fr	Sa
					1	2
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28	29	30

October						
Su	Mo	Tu	We	Th	Fr	Sa
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30	31				


November						
Su	Mo	Tu	We	Th	Fr	Sa
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30		

December						
Su	Mo	Tu	We	Th	Fr	Sa
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30	31					

Impact of TCR TT 2023 at Infrabel

Section Antwerpen-Montzen

Map view

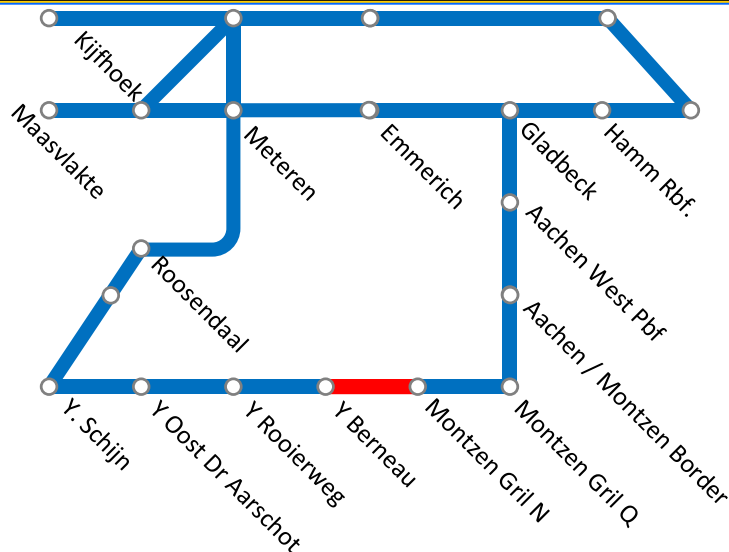

Impact on International Rail Freight

- Deviations: No
- Estimated extra running time: tbd
- Restrictions for ad-hoc requests: no
- Restrictions in train parameters: no
- Restrictions in container profile: No
- In annual timetable: no, timetables adapted at the latest 4 weeks before operation

Major Capacity Restriction

- Location: Y.Berneau – Fouron
- Single track operation
- Period: 04.09.2023 – 26.11.2023
- Assainissement

2023 Calendar


Single track operation Total closure

January							February							March							April						
Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa
1	2	3	4	5	6	7				1	2	3	4				1	2	3	4							1
8	9	10	11	12	13	14	5	6	7	8	9	10	11	5	6	7	8	9	10	11	2	3	4	5	6	7	8
15	16	17	18	19	20	21	12	13	14	15	16	17	18	12	13	14	15	16	17	18	9	10	11	12	13	14	15
22	23	24	25	26	27	28	19	20	21	22	23	24	25	19	20	21	22	23	24	25	16	17	18	19	20	21	22
29	30	31					26	27	28					26	27	28	29	30	31		23	24	25	26	27	28	29
																					30						
May							June							July							August						
Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa
	1	2	3	4	5	6					1	2	3							1							1
7	8	9	10	11	12	13	4	5	6	7	8	9	10	2	3	4	5	6	7	8	6	7	8	9	10	11	12
14	15	16	17	18	19	20	11	12	13	14	15	16	17	9	10	11	12	13	14	15	13	14	15	16	17	18	19
21	22	23	24	25	26	27	18	19	20	21	22	23	24	16	17	18	19	20	21	22	20	21	22	23	24	25	26
28	29	30	31				25	26	27	28	29	30		23	24	25	26	27	28	29	27	28	29	30	31		
														30	31												
September							October							November							December						
Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa
						1	1	2	3	4	5	6	7				1	2	3	4							1
3	4	5	6	7	8	9	8	9	10	11	12	13	14	5	6	7	8	9	10	11	3	4	5	6	7	8	9
10	11	12	13	14	15	16	15	16	17	18	19	20	21	12	13	14	15	16	17	18	10	11	12	13	14	15	16
17	18	19	20	21	22	23	22	23	24	25	26	27	28	19	20	21	22	23	24	25	17	18	19	20	21	22	23
24	25	26	27	28	29	30	29	30	31					26	27	28	29	30			24	25	26	27	28	29	30
																					31						

Impact of TCR TT 2023 at DB Netz AG

Section Emmerich Border - Oberhausen Main Station

Map view

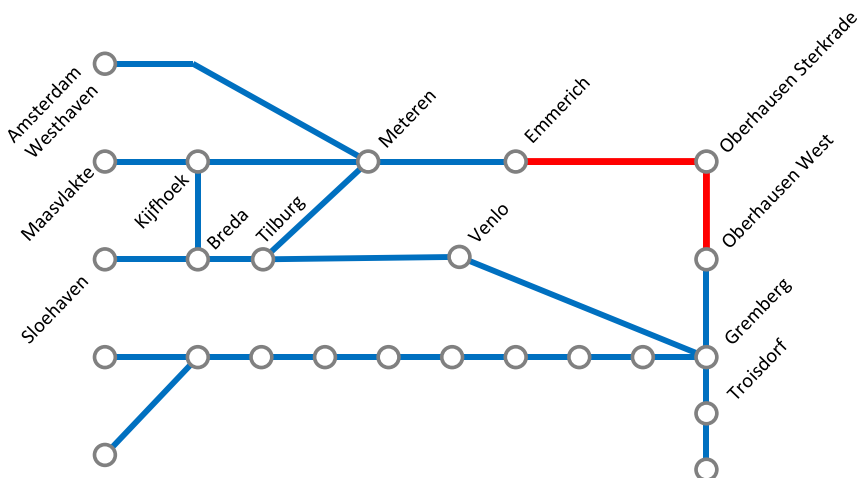

Impact on International Rail Freight c

- Cancellations: Yes
- Deviations: Yes
- Estimated extra running time: Detailed information on extra running time is distributed by DB Netz individually for every customer for each affected train. Additionally DB Netz offers train path advice free of charge
- In annual timetable: No

Major Capacity Restriction

- Emmerich Border - Oberhausen Main Station
- Type: Total Closure, Single Track Operation
- Period: Feb –Dec. 2023 (& 2024 ff.)
- Type of works: Track & Rail, Bridge, Catenary, Switch, Miscellaneous

2023 Calendar

Single track operation Total closure

January							February							March							April						
Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa
1	2	3	4	5	6	7				1	2	3	4				1	2	3	4							1
8	9	10	11	12	13	14	5	6	7	8	9	10	11	5	6	7	8	9	10	11	2	3	4	5	6	7	8
15	16	17	18	19	20	21	12	13	14	15	16	17	18	12	13	14	15	16	17	18	9	10	11	12	13	14	15
22	23	24	25	26	27	28	19	20	21	22	23	24	25	19	20	21	22	23	24	25	16	17	18	19	20	21	22
29	30	31					26	27	28					26	27	28	29	30	31		23	24	25	26	27	28	29
																					30						

May							June							July							August						
Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa
	1	2	3	4	5	6					1	2	3						1								5
7	8	9	10	11	12	13	4	5	6	7	8	9	10	2	3	4	5	6	7	8	6	7	8	9	10	11	12
14	15	16	17	18	19	20	11	12	13	14	15	16	17	9	10	11	12	13	14	15	13	14	15	16	17	18	19
21	22	23	24	25	26	27	18	19	20	21	22	23	24	16	17	18	19	20	21	22	20	21	22	23	24	25	26
28	29	30	31				25	26	27	28	29	30		23	24	25	26	27	28	29	27	28	29	30	31		

September							October							November							December						
Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa
					1	2	1	2	3	4	5	6	7														
3	4	5	6	7	8	9	8	9	10	11	12	13	14	5	6	7	8	9	10	11	3	4	5	6	7	8	9
10	11	12	13	14	15	16	15	16	17	18	19	20	21	12	13	14	15	16	17	18	10	11	12	13	14	15	16
17	18	19	20	21	22	23	22	23	24	25	26	27	28	19	20	21	22	23	24	25	17	18	19	20	21	22	23
24	25	26	27	28	29	30	29	30	31					26	27	28	29	30			24	25	26	27	28	29	30

December																											
Su	Mo	Tu	We	Th	Fr	Sa																					

Section Korsche Towarowa – Ełk Towarowy

A map view of the rail network. The main line runs from Frankfurt (O) to Trakiszki. A branch line connects Frankfurt (O) to Frankfurt (O) Hbf, which then connects to Dresden Friedrichstadt. Another branch line connects Frankfurt (O) to Berlin Koepenick, which then connects to Horka Hbf. A third branch line connects Frankfurt (O) to Poznań Starołęka, which then connects to Wrocław Brochów. A fourth branch line connects Frankfurt (O) to Inowrocław Tow., which then connects to Toruń Wschodni. A fifth branch line connects Frankfurt (O) to Poznań Starołęka, which then connects to Gdki. A sixth branch line connects Frankfurt (O) to Poznań Starołęka, which then connects to Swarzędz. A seventh branch line connects Frankfurt (O) to Poznań Starołęka, which then connects to Kutno. An eighth branch line connects Frankfurt (O) to Poznań Starołęka, which then connects to Łowicz. A ninth branch line connects Frankfurt (O) to Poznań Starołęka, which then connects to Skiemlewie. A tenth branch line connects Frankfurt (O) to Poznań Starołęka, which then connects to Pilawa. An eleventh branch line connects Frankfurt (O) to Poznań Starołęka, which then connects to Małaszewicze. A twelfth branch line connects Frankfurt (O) to Poznań Starołęka, which then connects to Suwalki. A thirteenth branch line connects Frankfurt (O) to Poznań Starołęka, which then connects to Olecko. A fourteenth branch line connects Frankfurt (O) to Poznań Starołęka, which then connects to Ełk Towarowy. A fifteenth branch line connects Frankfurt (O) to Poznań Starołęka, which then connects to Karsze Towarowy. A sixteenth branch line connects Frankfurt (O) to Poznań Starołęka, which then connects to Iława Gł.

Impact on International Rail Freight

- percentage of rerouting or cancellation: 100% rerouting due to total line closure
- extra running time for freight trains: tbd
- deviation: via Olsztyn – Szczytno - Ełk
- timetable: TT 2023 - 2025
- no restrictions in train parameters

Major Capacity Restriction

Location: Korsze Towarowa – Giżycko

Type:

- Total Line Closure, see calendar
- Renewal Works: Track & Rail, Catenary, Telecommunications, Signalling
- Duration: Continuous

Location: Korsze Towarowa – Giżycko

Type:

- Total Line Closure, see calendar
- Renewal Works: Track & Rail, Catenary, Telecommunications, Signalling
- Duration: Continuous

Section Korsche Towarowa – Elk Towarowy

Works : Renewal

 Single track operation  Total closure

KW	Mo	Ti	Mi	Do	Fr	Sa	So
1			1	2	3	4	5
2	6	7	8	9	10	11	12
3	13	14	15	16	17	18	19
4	20	21	22	23	24	25	26
5	27	28	29	30	31		

KW	Mo	Ti	Mi	Do	Fr	Sa	So
5						1	2
6	3	4	5	6	7	8	9
7	10	11	12	13	14	15	16
8	17	18	19	20	21	22	23
9	24	25	26	27	28	29	

KW	Mo	Ti	Mi	Do	Fr	Sa	So
9							1
10	2	3	4	5	6	7	8
11	9	10	11	12	13	14	15
12	16	17	18	19	20	21	22
13	23	24	25	26	27	28	29
14	30	31					

KW	Mo	Ti	Mi	Do	Fr	Sa	So
14			1	2	3	4	5
15	6	7	8	9	10	11	12
16	13	14	15	16	17	18	19
17	20	21	22	23	24	25	26
18	27	28	29	30			

KW	Mo	Ti	Mi	Do	Fr	Sa	So
18					1	2	3
19	4	5	6	7	8	9	10
20	11	12	13	14	15	16	17
21	18	19	20	21	22	23	24
22	25	26	27	28	29	30	31

KW	Mo	Ti	Mi	Do	Fr	Sa	So
23	1	2	3	4	5	6	7
24	8	9	10	11	12	13	14
25	15	16	17	18	19	20	21
26	22	23	24	25	26	27	28
27	29	30					

KW	Mo	Ti	Mi	Do	Fr	Sa	So
27			1	2	3	4	5
28	6	7	8	9	10	11	12
29	13	14	15	16	17	18	19
30	20	21	22	23	24	25	26
31	27	28	29	30	31		

KW	Mo	Ti	Mi	Do	Fr	Sa	So
31						1	2
32	3	4	5	6	7	8	9
33	10	11	12	13	14	15	16
34	17	18	19	20	21	22	23
35	24	25	26	27	28	29	30
36	31						

KW	Mo	Ti	Mi	Do	Fr	Sa	So
36		1	2	3	4	5	6
37	7	8	9	10	11	12	13
38	14	15	16	17	18	19	20
39	21	22	23	24	25	26	27
40	28	29	30				

KW	Mo	Ti	Mi	Do	Fr	S
----	----	----	----	----	----	---

Works : Renewal

 Single track operation

 Single track operation
 Total closure

January							
KW	Mo	Tu	We	Th	Fr	Sa	Su
1			1	2	3	4	5
2	6	7	8	9	10	11	12
3	13	14	15	16	17	18	19
4	20	21	22	23	24	25	26
5	27	28	29	30	31		

January							February								
KW	Mo	Tu	We	Th	Fr	Sa	So	KW	Mo	Tu	We	Th	Fr	Sa	So
1				1	2	3	4	5						1	2
2	6	7	8	9	10	11	12	13	3	4	5	6	7	8	9
3	13	14	15	16	17	18	19	20	10	11	12	13	14	15	16
4	20	21	22	23	24	25	26	27	17	18	19	20	21	22	23
5	27	28	29	30	31			28	19	20	21	22	23	24	25
									24	25	26	27	28	29	30

January							February							March												
kW	Mo	Tu	Di	Mi	Do	Fr	Sa	So	kW	Mo	Tu	Di	Mi	Do	Fr	Sa	So	kW	Mo	Tu	Di	Mi	Do	Fr	Sa	So
1				1	2	3	4	5	5							1	2	9								
2	6	7	8	9	10	11	12		6	3	4	5	6	7	8	9		10	2	3	4	5	6	7	8	9
3	13	14	15	16	17	18	19		7	10	11	12	13	14	15	16		11	9	10	11	12	13	14	15	16
4	20	21	22	23	24	25	26		8	17	18	19	20	21	22	23		12	16	17	18	19	20	21	22	23
5	27	28	29	30	31				9	24	25	26	27	28	29			13	23	24	25	26	27	28	29	30
																		14	30	31						

January							February							March							April											
KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	
1				1	2	3	4	5						1	2	6							1	7				1	2	3	4	
2	6	7	8	9	10	11	12	3	4	5	6	7	8	9		4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8
3	13	14	15	16	17	18	19	5	6	7	8	9	10	11	12	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23
4	20	21	22	23	24	25	26	6	7	8	9	10	11	12	13	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24
5	27	28	29	30	31			9	10	11	12	13	14	15	16	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25

January							February							March							April											
KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	
1				1	2	3	4	5						1	2	6							1	7				1	2	3	4	
2	6	7	8	9	10	11	12	3	4	5	6	7	8	9		4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8
3	13	14	15	16	17	18	19	5	6	7	8	9	10	11	12	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23
4	20	21	22	23	24	25	26	6	7	8	9	10	11	12	13	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24
5	27	28	29	30	31			9	10	11	12	13	14	15	16	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25

January							February							March							April											
KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	
1				1	2	3	4	5						1	2	6							1	7				1	2	3	4	
2	6	7	8	9	10	11	12	3	4	5	6	7	8	9		4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8
3	13	14	15	16	17	18	19	5	6	7	8	9	10	11	12	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23
4	20	21	22	23	24	25	26	6	7	8	9	10	11	12	13	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24
5	27	28	29	30	31			9	10	11	12	13	14	15	16	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25

January							February							March							April											
KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	
1				1	2	3	4	5						1	2	6							1	7				1	2	3	4	
2	6	7	8	9	10	11	12	3	4	5	6	7	8	9		4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8
3	13	14	15	16	17	18	19	5	6	7	8	9	10	11	12	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23
4	20	21	22	23	24	25	26	6	7	8	9	10	11	12	13	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24
5	27	28	29	30	31			9	10	11	12	13	14	15	16	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25

January							February							March							April											
KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	
1				1	2	3	4	5						1	2	6							1	7				1	2	3	4	
2	6	7	8	9	10	11	12	3	4	5	6	7	8	9		4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8
3	13	14	15	16	17	18	19	5	6	7	8	9	10	11	12	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23
4	20	21	22	23	24	25	26	6	7	8	9	10	11	12	13	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24
5	27	28	29	30	31			9	10	11	12	13	14	15	16	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25

January							February							March							April											
KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	
1				1	2	3	4	5						1	2	6							1	7				1	2	3	4	
2	6	7	8	9	10	11	12	3	4	5	6	7	8	9		4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8
3	13	14	15	16	17	18	19	5	6	7	8	9	10	11	12	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23
4	20	21	22	23	24	25	26	6	7	8	9	10	11	12	13	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24
5	27	28	29	30	31			9	10	11	12	13	14	15	16	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25

January							February							March							April											
KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	
1				1	2	3	4	5						1	2	6							1	7				1	2	3	4	
2	6	7	8	9	10	11	12	3	4	5	6	7	8	9		4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8
3	13	14	15	16	17	18	19	5	6	7	8	9	10	11	12	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23
4	20	21	22	23	24	25	26	6	7	8	9	10	11	12	13	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24
5	27	28	29	30	31			9	10	11	12	13	14	15	16	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25

January							February							March							April											
KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	
1				1	2	3	4	5						1	2	6							1	7				1	2	3	4	
2	6	7	8	9	10	11	12	3	4	5	6	7	8	9		4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8
3	13	14	15	16	17	18	19	5	6	7	8	9	10	11	12	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23
4	20	21	22	23	24	25	26	6	7	8	9	10	11	12	13	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24
5	27	28	29	30	31			9	10	11	12	13	14	15	16	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25

January							February							March							April											
KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	
1				1	2	3	4	5						1	2	6							1	7				1	2	3	4	
2	6	7	8	9	10	11	12	3	4	5	6	7	8	9		4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8
3	13	14	15	16	17	18	19	5	6	7	8	9	10	11	12	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23
4	20	21	22	23	24	25	26	6	7	8	9	10	11	12	13	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24
5	27	28	29	30	31			9	10	11	12	13	14	15	16	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25

January							February							March							April											
KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	KW	Mo	Tu	Wi	Th	Fr	Sa	So	
1				1	2	3	4	5						1	2	6							1	7				1	2	3	4	
2	6	7	8	9	10	11	12	3	4	5	6	7	8	9		4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8
3	13	14	15	16	17	18	19	5	6	7	8	9	10	11	12	7	8	9	10	11	12	13	14	15	16	17						

May							
KW	Mo	Tu	We	Th	Fr	Sa	Su
18					1	2	3
19	4	5	6	7	8	9	10
20	11	12	13	14	15	16	17
21	18	19	20	21	22	23	24
22	25	26	27	28	29	30	31

May							
kW	Mo	Tu	We	Th	Fr	Sa	So
18					1	2	3
19	4	5	6	7	8	9	10
20	11	12	13	14	15	16	17
21	18	19	20	21	22	23	24
22	25	26	27	28	29	30	31

June							
kW	Mo	Tu	We	Th	Fr	Sa	So
23	1	2	3	4	5	6	7
24	8	9	10	11	12	13	14
25	15	16	17	18	19	20	21
26	22	23	24	25	26	27	28
27	29	30					

May							June							July									
kW	Mo	Tu	We	Th	Fr	Sa	So	kW	Mo	Tu	We	Th	Fr	Sa	So	kW	Mo	Tu	We	Th	Fr	Sa	So
18						1	2	3								27	1	2	3	4	5	6	7
19	3	5	5	7	8	9	10	11	12	13	14	15	16	17	18	28	6	7	8	9	10	11	12
20	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	29	13	14	15	16	17	18	19
21	18	19	20	21	22	23	24	25	26	27	28	29	30	31		30	20	21	22	23	24	25	26
22	25	26	27	28	29	30	31									31	27	28	29	30	31		

May							June							July							August						
kW	Mo	Tu	We	Th	Fr	Sa	kW	Mo	Tu	We	Th	Fr	Sa	kW	Mo	Tu	We	Th	Fr	Sa	kW	Mo	Tu	We	Th	Fr	Sa
18							23	1	2	3	4	5	6	28	1	2	3	4	5		31						
19	3	5	6	7	8	9	24	6	9	10	11	12	13	29	6	7	8	9	10	11	32	3	4	5	6	7	8
20	11	12	13	14	15	16	25	15	16	17	18	19	20	30	13	14	15	16	17	18	33	10	11	12	13	14	15
21	18	19	20	21	22	23	26	22	23	24	25	26	27	31	20	21	22	23	24	25	34	17	18	19	20	21	22
22	25	26	27	28	29	30	27	29	30						27	28	29	30	31		35	24	25	26	27	28	29

September							
KW	Mo	Tu	We	Th	Fr	Sa	Su
36		1	2	3	4	5	6
37	7	8	9	10	11	12	13
38	14	15	16	17	18	19	20
39	21	22	23	24	25	26	27
40	28	29	30				

September							
kW	Mo	Ti	Mi	Do	Fr	Sa	So
36		1	2	3	4	5	6
37	7	8	9	10	11	12	13
38	14	15	16	17	18	19	20
39	21	22	23	24	25	26	27
40	28	29	30				

October							
kW	Mo	Ti	Mi	Do	Fr	Sa	So
40				1	2	3	4
41	5	6	7	8	9	10	11
42	12	13	14	15	16	17	18
43	19	20	21	22	23	24	25
44	26	27	28	29	30	31	

September							October							November									
KW	Mo	Tu	We	Th	Fr	Sa	Su	KW	Mo	Tu	We	Th	Fr	Sa	Su	KW	Mo	Tu	We	Th	Fr	Sa	Su
36		1	2	3	4	5	6	40		1	2	3	4	5	6	43		1	2	3	4	5	6
37	7	8	9	10	11	12	13	41	5	6	7	8	9	10	11	45	2	3	4	5	6	7	8
38	14	15	16	17	18	19	20	42	12	13	14	15	16	17	18	46	9	10	11	12	13	14	15
39	21	22	23	24	25	26	27	43	19	20	21	22	23	24	25	47	16	17	18	19	20	21	22
40	28	29	30					44	26	27	28	29	30	31		48	23	24	25	26	27	28	29
																49	30						

September							October							November							December						
KW	Mo	Tu	We	Th	Fr	Sa	KW	Mo	Tu	We	Th	Fr	Sa	KW	Mo	Tu	We	Th	Fr	Sa	KW	Mo	Tu	We	Th	Fr	Sa
36		1	2	3	4	5	40		1	2	3	4		44						1	48		1	2	3	4	
37	7	8	9	10	11	12	41	5	6	7	8	9	11	45	2	3	4	5	6	7	8	49	5	6	7	8	9
38	14	15	16	17	18	19	42	12	13	14	15	16	17	46	9	10	11	12	13	14	15	50	12	13	14	15	
39	21	22	23	24	25	26	43	19	20	21	22	23	24	47	16	17	18	19	20	21	22	51	14	15	16	17	
40	28	29	30				44	26	27	28	29	30	31	48	23	24	25	26	27	28	29	52	21	22	23	24	
														49	30							53	28	29	30	31	

Impact of TCR TT 2023 at PKP PLK

Section Zabrze Biskupice – Sosnowiec Jęzor

Map view



Impact on International Rail Freight

- percentage of rerouting or cancellation: 100% rerouting due to total line closure
- extra running time for freight trains: yes
- deviation: via lines no. 657 and 658
- timetable: TT 2023-2024
- no restrictions in train parameters

Major Capacity Restriction

Location: Szabelnia – Katowice Szopienice Północne

Type:

- Total Line Closure, see calendar
- Modernization: Track & Rail, Catenary, Telecommunications, Signalling
- Duration: Continuous

Section Korsche Towarowa - Elk Towarowy

Works : Renewal


Single track operation Total closure

January							February							March							April										
KW	Mo	Tu	We	Th	Fr	Sa	Su	KW	Mo	Tu	We	Th	Fr	Sa	Su	KW	Mo	Tu	We	Th	Fr	Sa	Su	KW	Mo	Tu	We	Th	Fr	Sa	Su
1			1	2	3	4	5	6						1	2	7							14			1	2	3	4	5	
2	6	7	8	9	10	11	12	6	3	4	5	6	7	8	9	10	2	3	4	5	6	7	8	15	6	7	8	9	10	11	12
3	13	14	15	16	17	18	19	7	10	11	12	13	14	15	16	11	9	10	11	12	13	14	15	16	13	14	15	16	17	18	19
4	20	21	22	23	24	25	26	8	17	18	19	20	21	22	23	12	16	17	18	19	20	21	22	17	20	21	22	23	24	25	26
5	27	28	29	30	31			9	24	25	26	27	28	29		13	23	24	25	26	27	28	29	18	27	28	29	30			
																14	30	31													
May							June							July							August										
KW	Mo	Tu	We	Th	Fr	Sa	Su	KW	Mo	Tu	We	Th	Fr	Sa	Su	KW	Mo	Tu	We	Th	Fr	Sa	Su	KW	Mo	Tu	We	Th	Fr	Sa	Su
18								23	1	2	3	4	5	6	7	24								31							
19	4	5	6	7	8	9	10	24	8	9	10	11	12	13	14	25	6	7	8	9	10	11	12	32	3	4	5	6	7	8	9
20	11	12	13	14	15	16	17	25	15	16	17	18	19	20	21	26	13	14	15	16	17	18	19	33	10	11	12	13	14	15	16
21	18	19	20	21	22	23	24	26	22	23	24	25	26	27	28	27	20	21	22	23	24	25	26	34	17	18	19	20	21	22	23
22	25	26	27	28	29	30	31	27	29	30						28	24	25	26	27	28	29	30	35	24	25	26	27	28	29	30
																29	31							36	31						
September							October							November							December										
KW	Mo	Tu	We	Th	Fr	Sa	Su	KW	Mo	Tu	We	Th	Fr	Sa	Su	KW	Mo	Tu	We	Th	Fr	Sa	Su	KW	Mo	Tu	We	Th	Fr	Sa	Su
36		1	2	3	4	5	6	40				1	2	3	4	44							1	49							
37	7	8	9	10	11	12	13	41	5	6	7	8	9	10	11	45	2	3	4	5	6	7	8	50	7	8	9	10	11	12	13
38	14	15	16	17	18	19	20	42	12	13	14	15	16	17	18	46	9	10	11	12	13	14	15	51	14	15	16	17	18	19	20
39	21	22	23	24	25	26	27	43	19	20	21	22	23	24	25	47	16	17	18	19	20	21	22	52	21	22	23	24	25	26	27
40	28	29	30					44	26	27	28	29	30	31		48	23	24	25	26	27	28	29	49	28	29	30	31			
																49	30														

Impact of a major TCR in 2023 and 2024 at LTG Infra

Section Žeimiai-Lukšiai

Map view

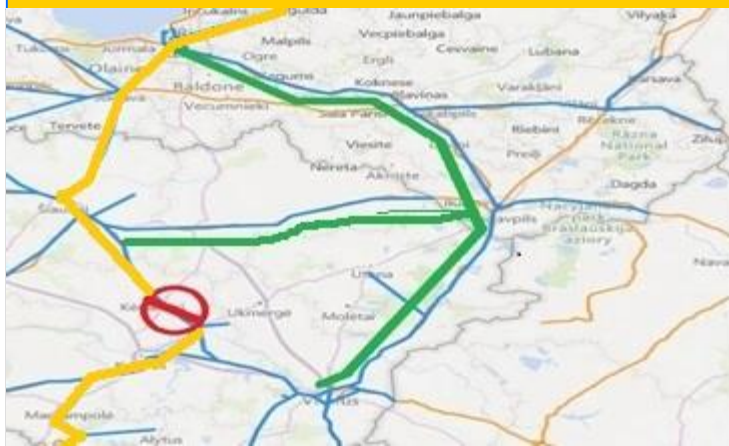

Impact on International Rail Freight

- percentage of rerouting or cancellation:
 - 10-15 % cancelled, rerouting via deviation line depends on the traffic volumes
- Deviations:
 - Vilnius-Turmantas-LV-Rokiškis-Radviliškis
- Restrictions in train parameters: no
- Restriction in container profiles: no

Major Capacity Restriction

Location: Žeimiai - Lukšiai


Type:

- Partial closure
- Period: continuous closure 01.2023 – 12.2024
- Works: Catenary installation
- **Benefit for RUs when the works are finalized:**
 - Electric traction
 - Heavier trains
 - Shorter running times
- **Impact on freight traffic during TCRs:**
 - 10-15 % trains is expected to be cancelled
 - rerouting possible via Vilnius-Turmantas-Latvia (Daugavpils)-Rokiškis-Radviliškis but necessity depends on the future traffic volumes
- **When coordination takes place with neighboring IMs and RUs?**
 - Before planning the works it was agreed with LDz to keep the deviation line open
 - Coordination with LDz about rerouting trains will take place, when exact number of affected trains will be known. The same with RUs.
- **When and how do RUs receive alternative timetable for the trains that were planned for the infected running days?**
 - Draft 2 months prior to the first day of works
 - Final 1 month prior to the first day of works

Impact of TCR TT 2024 at ProRail

Section Apeldoorn - Amersfoort

Map view

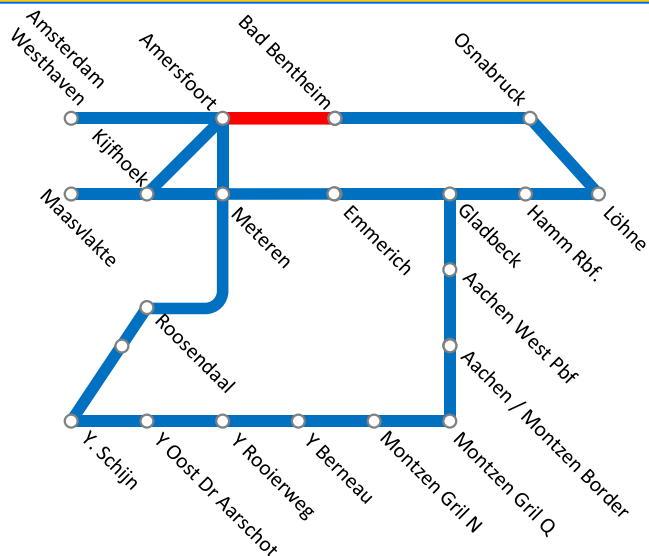

Impact on International Rail Freight

- Cancellations: no
- Deviations: national rerouting via Deventer – Arnhem, international rerouting via Emmerich - Meteren
- Estimated extra running time: 30 – 90 minutes
- In annual timetable: No

Major Capacity Restriction

- Amersfoort – Apeldoorn / Utrecht
- Type: Total Closure
- Period: see calendar
- Type of works: renewal infra lay out

2024 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7				1	2	3	4				1	2	3		1	2	3	4	5	6	7
8	9	10	11	12	13	14	5	6	7	8	9	10	11	4	5	6	7	8	9	10	8	9	10	11	12	13	14
15	16	17	18	19	20	21	12	13	14	15	16	17	18	11	12	13	14	15	16	17	15	16	17	18	19	20	21
22	23	24	25	26	27	28	19	20	21	22	23	24	25	18	19	20	21	22	23	24	22	23	24	25	26	27	28
29	30	31					26	27	28	29				25	26	27	28	29	30	31	29	30					


May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5						1	2	1	2	3	4	5	6	7	5	6	7	8	9	10	11
6	7	8	9	10	11	12	3	4	5	6	7	8	9	8	9	10	11	12	13	14	12	13	14	15	16	17	18
13	14	15	16	17	18	19	10	11	12	13	14	15	16	15	16	17	18	19	20	21	19	20	21	22	23	24	25
20	21	22	23	24	25	26	17	18	19	20	21	22	23	22	23	24	25	26	27	28	26	27	28	29	30	31	
27	28	29	30	31			24	25	26	27	28	29	30	29	30	31					29	30					

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
						1			1	2	3	4	5	4	5	6	7	8	9	10	3	4	5	6	7	8	
2	3	4	5	6	7	8	7	8	9	10	11	12	13	11	12	13	14	15	16	17	9	10	11	12	13	14	15
9	10	11	12	13	14	15	14	15	16	17	18	19	20	18	19	20	21	22	23	24	16	17	18	19	20	21	22
16	17	18	19	20	21	22	21	22	23	24	25	26	27	25	26	27	28	29	30		23	24	25	26	27	28	29
23	24	25	26	27	28	29	28	29	30	31				28	29	30					30	31					
30																											

Impact of TCR TT 2024 at ProRail

Section Hengelo - Bad Bentheim

Map view

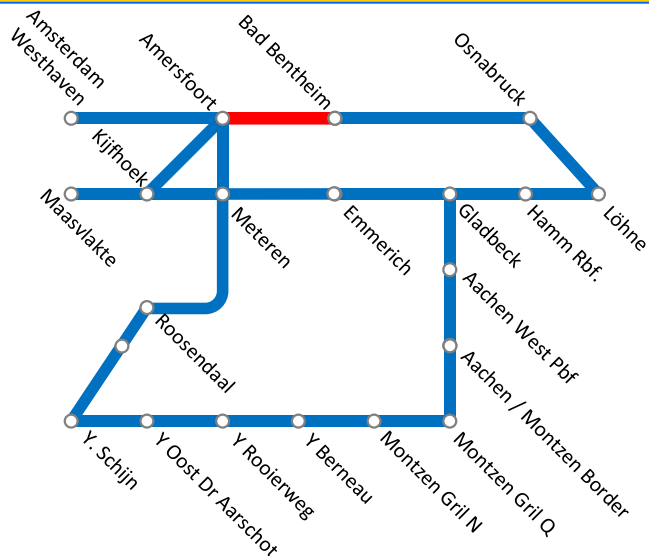

Impact on International Rail Freight

- Cancellations: no
- Deviations: international rerouting via Emmerich – Meteren or Kaldenkirchen - Venlo
- Estimated extra running time: 30 – 90 minutes
- In annual timetable: No

Major Capacity Restriction

- Hengelo
- Type: Total Closure
- Period: 23.09.2024 – 10.10.2024
- Type of works: renewal infra lay out

2024 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7				1	2	3	4					1	2	3	1	2	3	4	5	6	7
8	9	10	11	12	13	14	5	6	7	8	9	10	11	4	5	6	7	8	9	10	8	9	10	11	12	13	14
15	16	17	18	19	20	21	12	13	14	15	16	17	18	11	12	13	14	15	16	17	15	16	17	18	19	20	21
22	23	24	25	26	27	28	19	20	21	22	23	24	25	18	19	20	21	22	23	24	22	23	24	25	26	27	28
29	30	31					26	27	28	29				25	26	27	28	29	30	31	29	30					


May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5						1	2	1	2	3	4	5	6	7	5	6	7	8	9	10	11
6	7	8	9	10	11	12	3	4	5	6	7	8	9	8	9	10	11	12	13	14	12	13	14	15	16	17	18
13	14	15	16	17	18	19	10	11	12	13	14	15	16	15	16	17	18	19	20	21	19	20	21	22	23	24	25
20	21	22	23	24	25	26	17	18	19	20	21	22	23	22	23	24	25	26	27	28	26	27	28	29	30	31	
27	28	29	30	31			24	25	26	27	28	29	30	29	30	31											

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
						1												1	2	3	30	31					
2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10	2	3	4	5	6	7	8
9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17	9	10	11	12	13	14	15
16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24	16	17	18	19	20	21	22
23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30		23	24	25	26	27	28	29
30																					30	31					

Impact of TCR TT 2024 at Infrabel

Section Antwerpen - Montzen

Map view

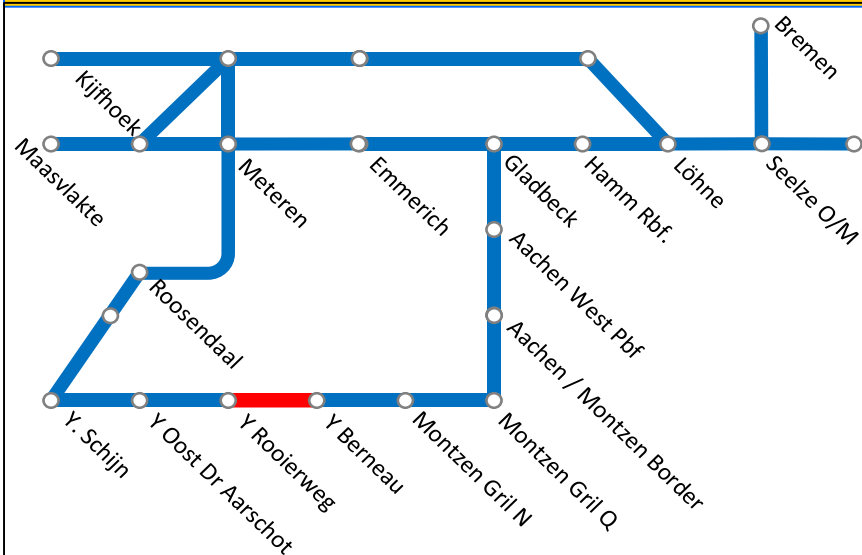

Impact on International Rail Freight

- percentage of rerouting or cancellation: 50% national rerouting
- extra running time for freight trains: 30'
- Deviation : L24/1-L40-L125B-L36A-L36
- In annual timetable: no, timetables adapted 4 weeks before operation
- Restrictions on train parameters: no
- Restriction in container profiles: no

Major Capacity Restriction

Location: Bassenge – Y. Glons

Type:

- Single track operation
- Works: Major works on bridge
- Duration: Continuous (15.04.2024 (7:00) – 09.06.2024 (22:00))

2024 Calendar

Single track operation Total closure


January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7				1	2	3	4					1	2	3	1	2	3	4	5	6	7
8	9	10	11	12	13	14	5	6	7	8	9	10	11	4	5	6	7	8	9	10	8	9	10	11	12	13	14
15	16	17	18	19	20	21	12	13	14	15	16	17	18	11	12	13	14	15	16	17	15	16	17	18	19	20	21
22	23	24	25	26	27	28	19	20	21	22	23	24	25	18	19	20	21	22	23	24	22	23	24	25	26	27	28
29	30	31					26	27	28	29				25	26	27	28	29	30	31	29	30					

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5						1	2	1	2	3	4	5	6	7	5	6	7	8	9	10	11
6	7	8	9	10	11	12	3	4	5	6	7	8	9	8	9	10	11	12	13	14	12	13	14	15	16	17	18
13	14	15	16	17	18	19	10	11	12	13	14	15	16	15	16	17	18	19	20	21	19	20	21	22	23	24	25
20	21	22	23	24	25	26	17	18	19	20	21	22	23	22	23	24	25	26	27	28	26	27	28	29	30	31	
27	28	29	30	31			24	25	26	27	28	29	30	29	30	31											

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
						1		1	2	3	4	5	6					1	2	3	30	31					
2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10	2	3	4	5	6	7	8
9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17	9	10	11	12	13	14	15
16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24	16	17	18	19	20	21	22
23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30		23	24	25	26	27	28	29
30																					30	31					

Impact of TCR TT 2024 at DB Netz AG

Section Emmerich Border - Oberhausen Main Station

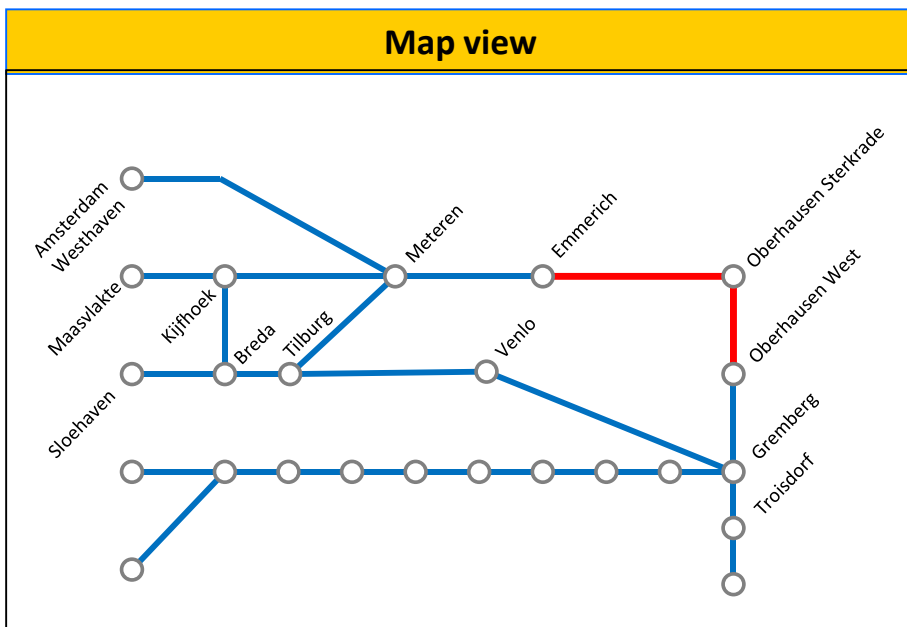

Impact on International Rail Freight

- Cancellations: Yes
- Deviations: Yes
- Estimated extra running time: Detailed information on extra running time is distributed by DB Netz individually for every customer for each affected train. Additionally DB Netz offers train path advice free of charge
- In annual timetable: No

Major Capacity Restriction

- Emmerich Border - Oberhausen Main Station
- Type: Single Track Operation (Until Oct only at night, from Nov on continuous) and Total Closures
- Period: Jan/Feb, May-Dec 2024 (& 2025 ff.)
- Type of works: Bridge, Track & Rail, Catenary, Switch, Miscellaneous

2024 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7	1	2	3	4	5	6	7	1	2	3	4	5	6	7	1	2	3	4	5	6	7
8	9	10	11	12	13	14	8	9	10	11	12	13	14	8	9	10	11	12	13	14	8	9	10	11	12	13	14
15	16	17	18	19	20	21	15	16	17	18	19	20	21	15	16	17	18	19	20	21	15	16	17	18	19	20	21
22	23	24	25	26	27	28	22	23	24	25	26	27	28	22	23	24	25	26	27	28	22	23	24	25	26	27	28
29	30	31					26	27	28	29				25	26	27	28	29	30	31	29	30					

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5						1	2											1	2	3	4
6	7	8	9	10	11	12	3	4	5	6	7	8	9	8	9	10	11	12	13	14	5	6	7	8	9	10	11
13	14	15	16	17	18	19	10	11	12	13	14	15	16	15	16	17	18	19	20	21	12	13	14	15	16	17	18
20	21	22	23	24	25	26	17	18	19	20	21	22	23	22	23	24	25	26	27	28	19	20	21	22	23	24	25
27	28	29	30	31			24	25	26	27	28	29	30	29	30	31					26	27	28	29	30	31	


September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
						1			1	2	3	4	5														1
2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10	2	3	4	5	6	7	8
9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17	9	10	11	12	13	14	15
16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24	16	17	18	19	20	21	22
23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30		23	24	25	26	27	28	29
30																					30	31					



Impact of TCR TT 2024 at DB Netz AG

Section Berlin Ostbahnhof – Frankfurt (Oder)

Map view

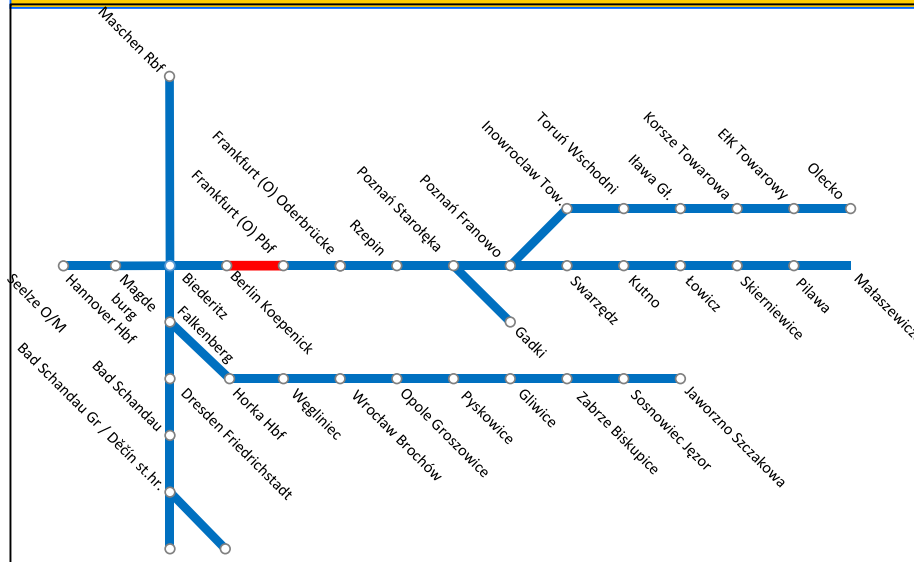

Impact on International Rail Freight

- Cancellations: Yes
- Deviations: Yes, e.g. via Cottbus – Berlin-Grünau – Eichgestell / Cottbus – Wünsdorf-Waldstadt – Diedersdorf
- Estimated extra running time: Detailed information on extra running time is distributed by DB Netz individually for every customer for each affected train. Additionally DB Netz offers train path advice free of charge
- In annual timetable: No

Major Capacity Restriction

- Location: Rahnsdorf Üst - Ostendgestell
- Type: Total closures
- Period: Jul 24 – Oct 24
- Works: Bridge

2024 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7				1	2	3	4					1	2	3	1	2	3	4	5	6	7
8	9	10	11	12	13	14	5	6	7	8	9	10	11	4	5	6	7	8	9	10	8	9	10	11	12	13	14
15	16	17	18	19	20	21	12	13	14	15	16	17	18	11	12	13	14	15	16	17	15	16	17	18	19	20	21
22	23	24	25	26	27	28	19	20	21	22	23	24	25	18	19	20	21	22	23	24	22	23	24	25	26	27	28
29	30	31					26	27	28	29				25	26	27	28	29	30	31	29	30					


May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5						1	2	1	2	3	4	5	6	7				1	2	3	4
6	7	8	9	10	11	12	3	4	5	6	7	8	9	8	9	10	11	12	13	14	5	6	7	8	9	10	11
13	14	15	16	17	18	19	10	11	12	13	14	15	16	15	16	17	18	19	20	21	12	13	14	15	16	17	18
20	21	22	23	24	25	26	17	18	19	20	21	22	23	22	23	24	25	26	27	28	19	20	21	22	23	24	25
27	28	29	30	31			24	25	26	27	28	29	30	29	30	31					26	27	28	29	30	31	

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
						1							1							1	2	3					
2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10	2	3	4	5	6	7	8
9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17	9	10	11	12	13	14	15
16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24	16	17	18	19	20	21	22
23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30		23	24	25	26	27	28	29
30																					30	31					

Impact of TCR TT 2024 at DB Netz AG

Section Dresden – Děčín (Elbe valley)

Map view

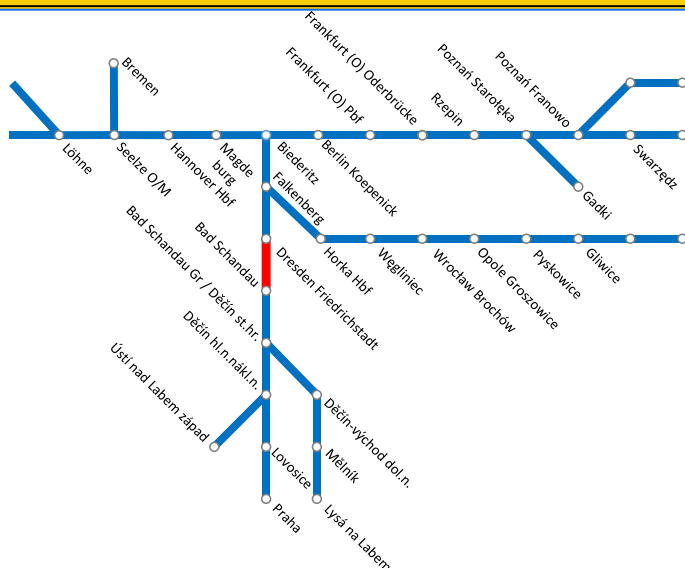

Impact on International Rail Freight

- Cancellations: Yes
- Deviations: No
- Estimated extra running time: Detailed information on extra running time is distributed by DB Netz individually for every customer for each affected train. Additionally DB Netz offers train path advice free of charge
- In annual timetable: Yes

Major Capacity Restriction

- Location: Schöna – Bad Schandau Ost
- Type: Single track operations and total closures
- Period: Dec 23 – Mar 24
- Duration: Continuous/Periodical
- Works: Bridge
- Total closures Mon: 08:50-16:40
- Total closures Wed/Fri: 06:30-07:30 + 16:30-17:30
- Additionally: Single track operations from 21st March to 12th December, Mon-Thu: 06:30-07:30 + 16:30-17:30

2024 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7	5	6	7	8	9	10	11	4	5	6	7	8	9	10	1	2	3	4	5	6	7
8	9	10	11	12	13	14	12	13	14	15	16	17	18	11	12	13	14	15	16	17	15	16	17	18	19	20	21
15	16	17	18	19	20	21	19	20	21	22	23	24	25	18	19	20	21	22	23	24	22	23	24	25	26	27	28
22	23	24	25	26	27	28	26	27	28	29				25	26	27	28	29	30	31	29	30					
29	30	31																									

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7	3	4	5	6	7	8	9	1	2	3	4	5	6	7	5	6	7	8	9	10	11
6	7	8	9	10	11	12	10	11	12	13	14	15	16	8	9	10	11	12	13	14	12	13	14	15	16	17	18
13	14	15	16	17	18	19	17	18	19	20	21	22	23	15	16	17	18	19	20	21	19	20	21	22	23	24	25
20	21	22	23	24	25	26	24	25	26	27	28	29	30	22	23	24	25	26	27	28	26	27	28	29	30	31	
27	28	29	30	31										29	30	31											

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7	1	2	3	4	5	6	7	1	2	3	4	5	6	7	1	2	3	4	5	6	7
2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10	2	3	4	5	6	7	8
9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17	9	10	11	12	13	14	15
16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24	16	17	18	19	20	21	22
23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30		23	24	25	26	27	28	29
30																					30	31					

Impact of TCR TT 2024 at PKP PLK

Section Zabrze Biskupice – Sosnowiec Jęzor

Map view



Impact on International Rail Freight

- percentage of rerouting or cancellation: 100% rerouting due to total line closure
- extra running time for freight trains: yes
- deviation: via lines no. 657 and 658
- timetable: TT 2023-2024
- no restrictions in train parameters

Major Capacity Restriction

Location: Szabelnia – Katowice Szopienice Północne

Type:

- Total Line Closure, see calendar
- Modernization: Track & Rail, Catenary, Telecommunications, Signalling
- Duration: Continuous

2024 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7	1	2	3	4				1	2	3					1	2	3	4	5	6	7
8	9	10	11	12	13	14	5	6	7	8	9	10	11	4	5	6	7	8	9	10	8	9	10	11	12	13	14
15	16	17	18	19	20	21	12	13	14	15	16	17	18	11	12	13	14	15	16	17	15	16	17	18	19	20	21
22	23	24	25	26	27	28	19	20	21	22	23	24	25	18	19	20	21	22	23	24	22	23	24	25	26	27	28
29	30	31					26	27	28	29				25	26	27	28	29	30	31	29	30					
May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5					1	2		1	2	3	4	5	6	7				1	2	3	4
6	7	8	9	10	11	12	3	4	5	6	7	8	9	8	9	10	11	12	13	14	5	6	7	8	9	10	11
13	14	15	16	17	18	19	10	11	12	13	14	15	16	15	16	17	18	19	20	21	12	13	14	15	16	17	18
20	21	22	23	24	25	26	17	18	19	20	21	22	23	22	23	24	25	26	27	28	19	20	21	22	23	24	25
27	28	29	30	31			24	25	26	27	28	29	30	29	30	31					26	27	28	29	30	31	
September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
						1		1	2	3	4	5	6				1	2	3								1
2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10	2	3	4	5	6	7	8
9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17	9	10	11	12	13	14	15
16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24	16	17	18	19	20	21	22
23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30		23	24	25	26	27	28	29
30																					30	31					

Impact of TCR TT 2024 at PKP PLK

Section Korsze Towarowa – Ełk Towarowy

Map view



Impact on International Rail Freight

- percentage of rerouting or cancellation: 100% rerouting due to total line closure
- extra running time for freight trains: tbd
- deviation: via Olsztyn – Szczytno - Ełk
- timetable: TT 2023 - 2025
- no restrictions in train parameters

Major Capacity Restriction

Location: Korsze Towarowa – Ełk Towarowy

Type:

- Total Line Closure, see calendar
- Renewal Works: Track & Rail, Catenary, Telecommunications, Signalling
- Duration: Continuous

2024 Calendar

Single track operation Total closure

January							February							March							April						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7	1	2	3	4				1	2	3					1	2	3	4	5	6	7
8	9	10	11	12	13	14	5	6	7	8	9	10	11	4	5	6	7	8	9	10	8	9	10	11	12	13	14
15	16	17	18	19	20	21	12	13	14	15	16	17	18	11	12	13	14	15	16	17	15	16	17	18	19	20	21
22	23	24	25	26	27	28	19	20	21	22	23	24	25	18	19	20	21	22	23	24	22	23	24	25	26	27	28
29	30	31					26	27	28	29				25	26	27	28	29	30	31	29	30					

May							June							July							August						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5					1	2		1	2	3	4	5	6	7				1	2	3	4
6	7	8	9	10	11	12	3	4	5	6	7	8	9	8	9	10	11	12	13	14	5	6	7	8	9	10	11
13	14	15	16	17	18	19	10	11	12	13	14	15	16	15	16	17	18	19	20	21	12	13	14	15	16	17	18
20	21	22	23	24	25	26	17	18	19	20	21	22	23	22	23	24	25	26	27	28	19	20	21	22	23	24	25
27	28	29	30	31			24	25	26	27	28	29	30	29	30	31					26	27	28	29	30	31	

September							October							November							December						
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su
						1		1	2	3	4	5	6				1	2	3								1
2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10	2	3	4	5	6	7	8
9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17	9	10	11	12	13	14	15
16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24	16	17	18	19	20	21	22
23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30		23	24	25	26	27	28	29
30																					30	31					

Impact of TCR TT 2025 at Infrabel

Section Antwerpen - Montzen

Map view



Impact on International Rail Freight

- Deviations: via L40,L36A,L36
- Estimated extra running time: tbd
- Restrictions for ad-hoc requests: no
- Restrictions in train parameters: no
- Restrictions in container profile: No
- In annual timetable: No

Major Capacity Restriction

- Location: Hasselt – Y. Glons
- Total Closure
- Period: 08.11.2025 (0:00) – 17.11.2025 (04:00)
- Switches Renewal and Underpass construction

2025 Calendar

Single track operation Total closure

January						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		

February						
Mo	Tu	We	Th	Fr	Sa	Su
					1	2
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28		

March						
Mo	Tu	We	Th	Fr	Sa	Su
					1	2
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28	29	30
31						

April						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30				

May						
Mo	Tu	We	Th	Fr	Sa	Su
			1	2	3	4
5	6	7	8	9	10	11
12	13	14	15	16	17	18
19	20	21	22	23	24	25
26	27	28	29	30	31	

June						
Mo	Tu	We	Th	Fr	Sa	Su
						1
2	3	4	5	6	7	8
9	10	11	12	13	14	15
16	17	18	19	20	21	22
23	24	25	26	27	28	29
30						

July						
Mo	Tu	We	Th	Fr	Sa	Su
	1	2	3	4	5	6
7	8	9	10	11	12	13
14	15	16	17	18	19	20
21	22	23	24	25	26	27
28	29	30	31			

August						
Mo	Tu	We	Th	Fr	Sa	Su
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	31

September						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30					

October						
Mo	Tu	We	Th	Fr	Sa	Su
		1	2	3	4	5
6	7	8	9	10	11	12
13	14	15	16	17	18	19
20	21	22	23	24	25	26
27	28	29	30	31		


November						
Mo	Tu	We	Th	Fr	Sa	Su
					1	2
3	4	5	6	7	8	9
10	11	12	13	14	15	16
17	18	19	20	21	22	23
24	25	26	27	28	29	30

December						
Mo	Tu	We	Th	Fr	Sa	Su
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30	31				

Impact of TCR TT 2025 at DB Netz AG

Section Emmerich Border - Oberhausen Main Station

Map view

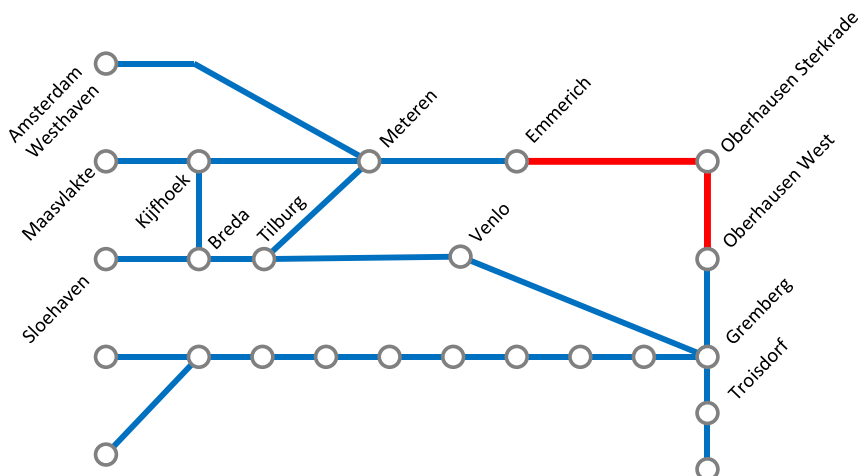

Impact on International Rail Freight

- Cancellations: Yes
- Deviations: Yes
- Estimated extra running time: Detailed information on extra running time is distributed by DB Netz individually for every customer for each affected train. Additionally DB Netz offers train path advice free of charge
- In annual timetable: Partly (2-month total closure Jun – Aug)

Major Capacity Restriction

- Location: Emmerich Border - Oberhausen Main Station
- Type: Total Closure, Single Track Operation
- Period: Jan – Dec 2025 (& 2026 ff.)
- Type of works: Track & Rail, Bridge, Catenary, Switch, Miscellaneous

2025 Calendar

Single track operation Total closure

January							February							March							April										
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su				
		1	2	3	4	5						1	2						1	2						1	2	3	4	5	6
6	7	8	9	10	11	12	3	4	5	6	7	8	9	3	4	5	6	7	8	9	7	8	9	10	11	12	13	14	15	16	
13	14	15	16	17	18	19	10	11	12	13	14	15	16	10	11	12	13	14	15	16	14	15	16	17	18	19	20	21	22	23	
20	21	22	23	24	25	26	17	18	19	20	21	22	23	17	18	19	20	21	22	23	21	22	23	24	25	26	27	28	29	30	
27	28	29	30	31			24	25	26	27	28			24	25	26	27	28	29	30	28	29	30								

May							June							July							August										
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su				
				1	2	3	4						1													1	2	3	4	5	6
5	6	7	8	9	10	11	2	3	4	5	6	7	8	7	8	9	10	11	12	13	4	5	6	7	8	9	10	11	12	13	
12	13	14	15	16	17	18	9	10	11	12	13	14	15	14	15	16	17	18	19	20	11	12	13	14	15	16	17	18	19	20	
19	20	21	22	23	24	25	16	17	18	19	20	21	22	21	22	23	24	25	26	27	18	19	20	21	22	23	24	25	26	27	
26	27	28	29	30	31		23	24	25	26	27	28	29	28	29	30	31				25	26	27	28	29	30	31				
							30																								

September							October							November							December											
Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su	Mo	Tu	We	Th	Fr	Sa	Su					
	1	2	3	4	5	6				1	2	3	4	5					1	2							1	2	3	4	5	6
8	9	10	11	12	13	14	6	7	8	9	10	11	12	3	4	5	6	7	8	9	1	2	3	4	5	6	7	8	9	10	11	
15	16	17	18	19	20	21	13	14	15	16	17	18	19	10	11	12	13	14	15	16	8	9	10	11	12	13	14	15	16	17	18	
22	23	24	25	26	27	28	20	21	22	23	24	25	26	17	18	19	20	21	22	23	15	16	17	18	19	20	21	22	23	24	25	
29	30						27	28	29	30	31			24	25	26	27	28	29	30	22	23	24	25	26	27	28	29	30	31		
